

Custom. Mt Black.


Work Order ID 160226

160226

Page 1

Monday, April 24, 2017 3:10:53 PM

Item ID: D4017-041MB Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Short Basket Base Assembly (350), Matte Black
 Start Date: 5/2/2017 Start Qty: 1.00 ***1*** Cust Item ID:
 Required Date: 5/8/2017 Req'd Qty: 1.00 ***1*** Customer:
 Reference: SCHEDULED/C MAT BLACK

Approvals: Process Plan:  Date: **APR 24 2017** Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D4017	E
D4020	A

100 Weld per dwg A/R S.S. rod Batch: **136920** 0.00

100

Large Fab

Large Fab

Memo

2.77

1- assemble ribs , weld as per dwg D4017 using DT9610B

inspect before welding mesh

2- Cut mesh as per dwg D4020-3

3- tack weld mesh on basket as per dwg D4017 and trim mesh to fit if necessary and trim to clear fasteners holes on the ends

4- weld hinge (3) and Mounting brackets as per dwg D4017

take lid to locate hinge and bracket

5- Weld D4672-3 blanking plates as per dwg

10 CP 17-05-25

110 QC9- Inspect visual per QSI004- Fusion Welds 0.00

110

QC

Quality Control

Memo

0.00

17-05-30 DAS
9
9-89

DTU

DQA:

Date:

JUN 20 2017

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed:

Date:

Work Order update only

Work Order: <u>160226</u> Part No. <u>D4017-041MB</u> NCR No. <u>17-6462</u>		DISPOSITION Rework ☒ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width:100%;"> <tr> <td>Skid-tube ☐</td> <td>Cross tube ☐</td> <td>Water Jet ☐</td> <td>Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☒</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☒	Composite ☐	Supplier ☐																																																									
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																																																																														
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																																																																														
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																																																																														
Large Fab ☒	Composite ☐	Supplier ☐																																																																															
Date: <u>17-05-30</u>		Step #: <u>100</u>		QTY Effective: <u>(1)</u>			MRB (QSI042) Approval DAS 9 <u>17-05-30</u>																																																																										
Description Work Order Deviation				Disposition				Completed By <u>C. 17-05-30</u>																																																																									
found at inspection that welds inside frame was missing. P.C. employee not re verifying is work and rushing.				weld missing areas.				Lead hand / Supervisor Approval Verification DAS 24 9-89 <u>17-05-30</u>																																																																									
								QC / QA Coordinator DAS Approval 9 9-89 <u>17-05-30</u>																																																																									
Root Cause <table style="width:100%;"> <tr> <td>Environment ☐</td> <td>No Re-verification ☐</td> <td>Pressure/Forced ☐</td> <td>Temperature/Cure ☐</td> <td>Power Loss/Surge ☐</td> <td>Positioned Wrong ☐</td> </tr> <tr> <td>Design ☐</td> <td>Operator ☐</td> <td>Bending ☐</td> <td>Set-up ☐</td> <td>Folio/Program ☐</td> <td>Outside Dimensions ☐</td> </tr> <tr> <td>Doc/Data ☐</td> <td>Offset/Setup ☐</td> <td>Centre Not Concentric ☐</td> <td>BOM/Route ☐</td> <td>Grain ☐</td> <td>Over/Under tolerance ☐</td> </tr> <tr> <td>Equip/Tooling ☐</td> <td>Supplier ☐</td> <td>Cracks ☐</td> <td>Broken/Damage/Defect ☐</td> <td>☒ Weld</td> <td>Part Incorrect ☐</td> </tr> <tr> <td>Handling/Pre ☐</td> <td>Training ☐</td> <td>Crimp/Kink/Ripple/Wave ☐</td> <td>Inspection Incomplete/Unqualified ☐</td> <td>Wrong Stock Pulled ☐</td> <td>Part Lost/Missing ☐</td> </tr> <tr> <td>Material ☐</td> <td>Use for Testing ☐</td> <td>Cuffs ☐</td> <td>Contamination ☐</td> <td>Out of Sequence ☐</td> <td>Part Moved ☐</td> </tr> <tr> <td>Internal Transport ☐</td> <td>Poor Information ☐</td> <td>Crushing ☐</td> <td>Countersink ☐</td> <td>Off-set ☐</td> <td>Drawing ☐</td> </tr> <tr> <td>Tribal Knowledge ☐</td> <td>☒ Rushing</td> <td>Heat Treat ☐</td> <td>Cut Too Short ☐</td> <td>Mislabeled ☐</td> <td>Finish ☐</td> </tr> <tr> <td>LOA ☐</td> <td>Product Improvement ☐</td> <td>Wave/Twist in Tube ☐</td> <td>Instructions Incomplete/Unclear ☐</td> <td>Fit/Function ☐</td> <td>Misread ☐</td> </tr> <tr> <td>Substation ☐</td> <td>Process Improvement ☐</td> <td>Marks/Chatter ☐</td> <td>Drill Holes ☐</td> <td>Misaligned/off center ☐</td> <td>Turning Sequence ☐</td> </tr> <tr> <td>Past Expiry Date ☐</td> <td>Manufacturing Process ☐</td> <td colspan="4"></td> </tr> <tr> <td>Misidentified ☐</td> <td>Past Due ☐</td> <td colspan="4">OTHER :</td> </tr> </table>				Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	☒ Weld	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	☒ Rushing	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐					Misidentified ☐	Past Due ☐	OTHER :									
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																																																																												
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																																																																												
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																																																																												
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	☒ Weld	Part Incorrect ☐																																																																												
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																																																																												
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																																																																												
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐																																																																												
Tribal Knowledge ☐	☒ Rushing	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐																																																																												
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																																																																												
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																																																																												
Past Expiry Date ☐	Manufacturing Process ☐																																																																																
Misidentified ☐	Past Due ☐	OTHER :																																																																															

Work Order ID 160226

Monday, April 24, 2017 3:10:53 PM

160226

Page 2

Item ID: D4017-041MB

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 5/8/2017 Req'd Qty: 1.00 ***1***

Customer:

Reference: SCHEDULED/C MAT BLACK

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC5- Inspect part completeness to step on W/O	0.00							DAS 9 9-89
120									
QC	Memo	0.02							
Quality Control									
125	Pressure Wash per QSI005 4.3	0.00							DAS 34 9-89
125									
HandFinish	Memo	0.36							
Hand Finishing									
130		0.00							DAS 41 9-89
130									
SprayPaint	Memo	0.00							
Spray Painting	1- Plug holes and mask only interior of hinge (3) prior to powder coat								
	Prime per QSI 005 4.2.1								
	Batch: <u>136772</u>								
	Paint Matte Black as per QSI005 4.2.2								
	Batch: <u>135519</u>								

MAY 31 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QS1042) Approval		
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	

Root Cause			FAULT CATEGORY			
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____				
Misidentified ☐	Past Due ☐					

Work Order ID 160226

Monday, April 24, 2017 3:10:53 PM

160226

Page 3

Item ID: D4017-041MB

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 5/8/2017 Req'd Qty: 1.00 ***1***

Customer:

Reference: SCHEDULED/C MAT BLACK

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
140	QC14- Inspect Spray Paint	0.00							
140									
QC	Memo	0.01							
Quality Control									EB 17-06-01
150	Assemble as per dwg	0.00							
150									
HandFinish	Memo	0.63							
Hand Finishing									11 f 170606
160	QC5- Inspect part completeness to step on W/O	0.00							
160									
QC	Memo	0.02							
Quality Control									DAS 38 9-89 JUN 01 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Work Order ID 160226

Monday, April 24, 2017 3:10:53 PM

160226

Page 4

Item ID: D4017-041MB Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Short Basket Base Assembly (350), Matte Black
Start Date: 5/2/2017 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 5/8/2017 Req'd Qty: 1.00 ***1*** Customer:
Reference: SCHEDULED/C MAT BLACK

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
170	Identify as per dwg & Stock Location: <u>w/o</u>	0.00							
170									
Packaging	Memo	0.01							
Packaging									
180	QC21- Final Inspection - Work Order Release	0.00							
180									
QC	Memo	0.10							
Quality Control									



JUN 01 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Picklist Print

Monday, April 24, 2017 3:10:52 PM

Page 1

Work Order ID: 160226

160226

Parent Item: D4017-041MB

D4017-041MR

Parent Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017

Required Date: 5/8/2017

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP RevA: new issue DD 09.11.30 verified by:EC IPP Rev:B as per dwg RevA DD 10.03.06 verified by:EC IPP Rev:C as per dwg RevB DD 10.04.16 verified by:EC IPP Rev:D as per dwg revC DD 10.08.18 verified by:EC IPP Rev:E 10.11.04 added pressure wash DD verf:EC IPP REV:F 12.07.24 AS PER DWG REV.D DD VERF:EC IPP REV:G 13.08.21 DWG REV.E / ECN 13-624 DD VERF:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D4021-5MB		Manufactured	No			150	Each	0.0000	2	2			
D4021-5MR									**				
Blanking Plate, Matte Black													
D4672-3		Manufactured	No			100	Each	34.0000	2	2			
D4672-3									**				
Blanking Plate													
Location Loc Qty Loc Code													
WA004 34													
141230 4													
157868 30													
M304EX0.75-16F		Purchased	No			100	sf	432.5000	19.1516	19.1516			
M304FX0 75-16F									**				
Expanded Metal Flat SS													
Location Loc Qty Loc Code													
WA004 432.5													
M136991 30.5													
M137294 402													

B160229 (2x) 17/06/01

B157868 (2) 17/06/01

B137491 → 20 17-06-02

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	
OTHER : _____					

Picklist Print

Monday, April 24, 2017 3:10:52 PM

Page 2

Work Order ID: 160226

160226

Parent Item: D4017-041MB

D4017-041MR

Parent Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017

Required Date: 5/8/2017

Start Qty: 1.00

Required Qty: 1.00

D4017-1 Manufactured No

100 Each 12.0000 1 1

✓ ***D4017-1***
Rib

B148052 → 1x Cg 17-05-24

Location Loc Qty Loc Code

WA004 12
144884 1
148052 11

D4017-3 Manufactured No

100 Each 4.0000 1 1

✓ ***D4017-3***
Rib

B160505 → 1x Cg 17-05-24

Location Loc Qty Loc Code

WA004 4
148053 4

D4017-5 Manufactured No

100 Each 10.0000 1 1

✓ ***D4017-5***
Hinge Rib

B157843 → 1x Cg 17-05-24

Location Loc Qty Loc Code

WA004 10
155747 2
157843 8

✓ D4017-7 Manufactured No

100 Each 10.0000 3 3

✓ ***D4017-7***
Rib

B160510 → 3x Cg 17-05-24

Location Loc Qty Loc Code

WA004 10
158860 10

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	
OTHER : _____					

Monday, April 24, 2017 3:10:52 PM

Required Qty: 1.00

4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

Picklist Print

Monday, April 24, 2017 3:10:52 PM

Page 4

Work Order ID: 160226

160226

Parent Item: D4017-041MB

D4017-041MB

Parent Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017

Required Date: 5/8/2017

Start Qty: 1.00

Required Qty: 1.00

D4034-043

Manufactured No

100

Each

5.0000

1

1

✓ ***D4034-043***

Fwd Upper Rib Assembly

**** B161538 → 1x Cy 17-05-30**

Location

Loc Qty

Loc Code

WA004

5

153910

1

157739

4

D2581

Manufactured No

100

Each

84.0000

2

2

✓ ***D2581***

Mounting Bracket

**** B152803 → 2x Cy 17-05-30**

Location

Loc Qty

Loc Code

WA004

84

152803

38

157620

26

159116

20

✓ D3913-15

Manufactured No

100

Each

19.0000

1

1

D3913-15

Wide Handle Plate

**** B157671 → 1x Cy 17-05-30**

Location

Loc Qty

Loc Code

WA004

19

157671

19

✓ D4016-1

Manufactured No

100

Each

69.0000

3

3

D4016-1

Hinge Half, Base

**** B158630 → 3x Cy 17-05-30**

Location

Loc Qty

Loc Code

WA004

69

154145

17

155346

12

158630

40

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Picklist Print

Monday, April 24, 2017 3:10:53 PM

Work Order ID: 160226

160226

Parent Item: D4017-041MB

D4017-041MR

Parent Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017

Required Date: 5/8/2017

Start Qty: 1.00

Required Qty: 1.00

✓ D4020-11

Manufactured No

100

Each

21.0000

2

2

D4020-11

End Mesh, Basket

**

B161475 → 2x G 17-05-30

Location

Loc Qty

Loc Code

WA004

21

152541

1

154521

2

156918

10

157499

8

D2931

Manufactured No

150

Each

1,366.000

2

2

D2931

Bumper

**

50 MAY 31 2017

Location

Loc Qty

Loc Code

ST013

66

86435

66

ST025A

1300

86435

1300

✓ D4021-1

Manufactured No

100

Each

45.0000

3

3

D4021-1

Handle Plate

**

B157523 → 3x G 17-05-30

Location

Loc Qty

Loc Code

WA004

45

157523

30

159375

15

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			Completed By
					Lead hand / Supervisor Approval Verification
					QC / QA Coordinator Approval
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Picklist Print

Monday, April 24, 2017 3:10:53 PM

Page 6

Work Order ID: 160226

160226

Parent Item: D4017-041MB

D4017-041MB

Parent Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017

Required Date: 5/8/2017

Start Qty: 1.00

Required Qty: 1.00

AN3-10A Purchased No

150 Each 228.0000 6 6

AN3-10A

Bolt

**

SD

MAY 31 2017

Location

Loc Qty

Loc Code

GA

60

m136787

60

ST349

168

m137321

168

NAS1149DN832J

Purchased No

150 Each 746.0000 2 2

NAS1149DN832.J

Washer

**

SD

MAY 31 2017

Location

Loc Qty

Loc Code

ST264

746

M135297

746

MS20600-AD4W3

Purchased No

150 Each 214.0000 2 2

MS20600-AD4W3

Cherry Rivet

**

2

DAS
6

9-89

MAY 31 2017

Location

Loc Qty

Loc Code

ST308

154

m135603

154

WA003

60

m136648

60

2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : _____									

Picklist Print

Monday, April 24, 2017 3:10:53 PM

Page 7

Work Order ID: 160226

160226

Parent Item: D4017-041MB

D4017-041MB

Parent Item Name: Short Basket Base Assembly (350), Matte Black

Start Date: 5/2/2017

Required Date: 5/8/2017

Start Qty: 1.00

Required Qty: 1.00

MS21042L3

Purchased

No

150

Each

2,031.000

6

6

MS21042L3

sel MAY 31 2017

Nut

Location

Loc Qty

Loc Code

FP001

100

m135945

100

GA

168

m134360

102

M136665

66

OVER007

300

m134360

0

M136665

300

ST303

1463

m137073

11

m137166

452

m137321

1000

137495

NAS1149F0332P

Purchased

No

150

Each

1,377.000

12

12

NAS1149F0332P

sel

Washer

Location

Loc Qty

Loc Code

GA

275

m133709

275

ST262

1102

m136835

8

m137075

1094

137412

MAY 31 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____


Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step # : _____		QTY Effective : _____			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : ☐									

ITEM	QTY -041	P/N	DESCRIPTION
	X	D4017-041	SHORT BASKET ASSY (350)
1	1	D4017-101	TUBULAR ASSY (350 SHORT BASKET)
2	2	D2581	MOUNTING BRACKET
3	2	D2831	BUMPER
4	1	D3913-15	WIDE HANDLE PLATE
5	3	D4016-1	HINGE HALF, BASE
6	1	D4020-3	MESH (350 BASKET SHORT BASE)
7	2	D4020-11	END MESH, BASKET
8	3	D4021-1	HANDLE PLATE
9	2	D4021-5	BLANKING PLATE
10	2	D4672-3	BLANKING PLATE
11	6	AN3-10A	BOLT, MACHINE
12	2	AN960JD8	WASHER
13	2	MS20600AD4W3	RIVET, BLIND, PAN-HEAD
14	6	MS21042L3	NUT, SELF-LOCKING
15	12	NAS1149F0332P	WASHER

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 160226

APR 24 2017

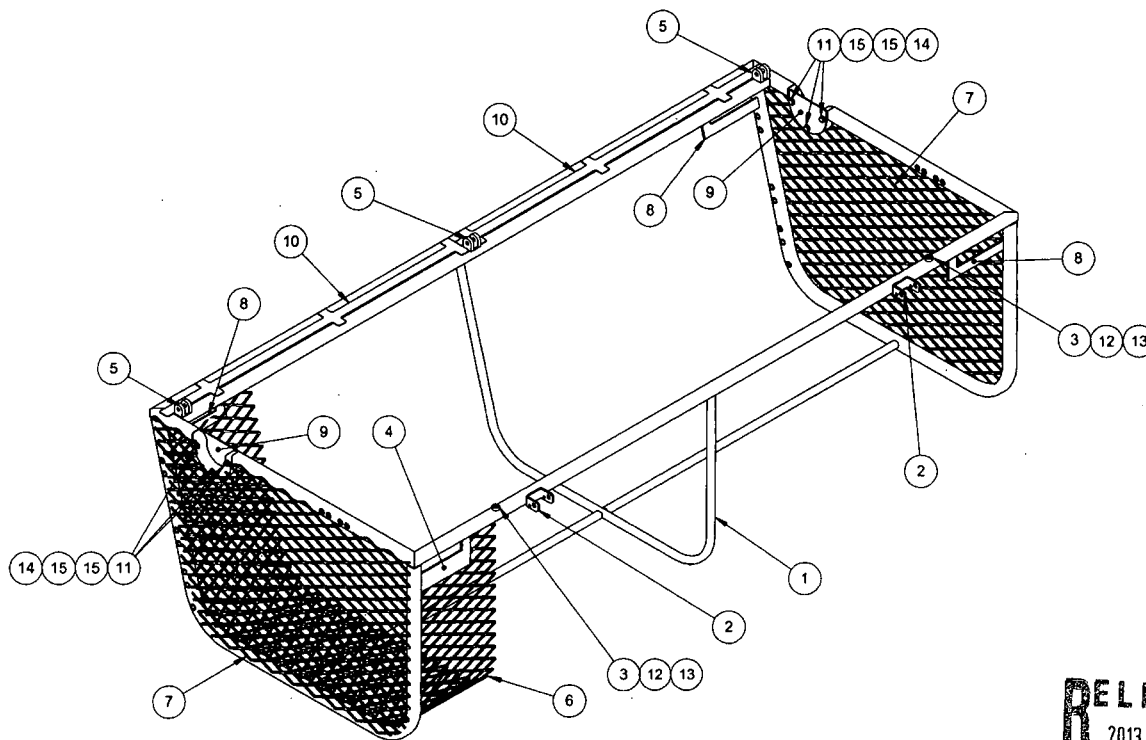

D4017-041 SHORT BASKET BASE ASSY (350)
(MESH SHOWN LOCALLY FOR CLARITY)

RELEASED
2013-08-16

- NOTES:
- 1) MATERIAL: N/A
 - 2) FINISH: POWDER COAT WHITE (4.3.5.2) PER DART QSI 005 4.3
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: N/A
 - 6) IDENTIFICATION: NONE
 - 7) WEIGHT: 28.8 lbs APPROX
 - 8) INSTALL AFTER FINISH
 - 9) MASK HOLES PRIOR TO POWDER COAT
 - 10) WELD PER DART QSI 004

E	PICTORIAL UPDATE TO MULTIPLE VIEWS FOR CHANGES TO D4034-043. A4-4 28.13 DIM IS NOW REF.	AJS	13.07.18
D	ADD D4672-3 (ZN C5-1, D4-1, D6-1, D3-2, AND D4-2). REASON: PAR12-197.	MB	12.06.18
C	ITEM #4 NOW INSTALLED OUTBOARD (C4-1, C5-1, B5-2 AND D6-2). REASON: ELIMINATE INTERFERENCE PREVENTING INSTALLATION OF RECEIVER ASSEMBLIES.	MB	10.07.23
B	QTY 1 D4021-1 REPLACED WITH QTY 1 D3913-15; AN3-10A BOLT WAS AN3C10A; NAS1149F0332P WASHER WAS NAS1149C0332R; SECTION F-F UPDATED (D6-2); ITEMS RENUMBERED; DETAIL D UPDATED (A4-3)	JPH	10.03.25
A	NEW ISSUE	AJS	10.03.04
REV.	DESCRIPTION	BY	DATE
DESIGN	AJS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA DRAWING NO. D4017 TITLE SHORT BASKET BASE ASSY (350) COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR FOR DISSEMINATION TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
DRAWN	AJS		
CHECKED			
MFG. APPR.			
APPROVED			
DE APPR.			
DATE	13.07.18		
		REV. E	SHEET 1 OF 5
		SCALE	NTS

8

7

6

5

4


3

2


1

D

D

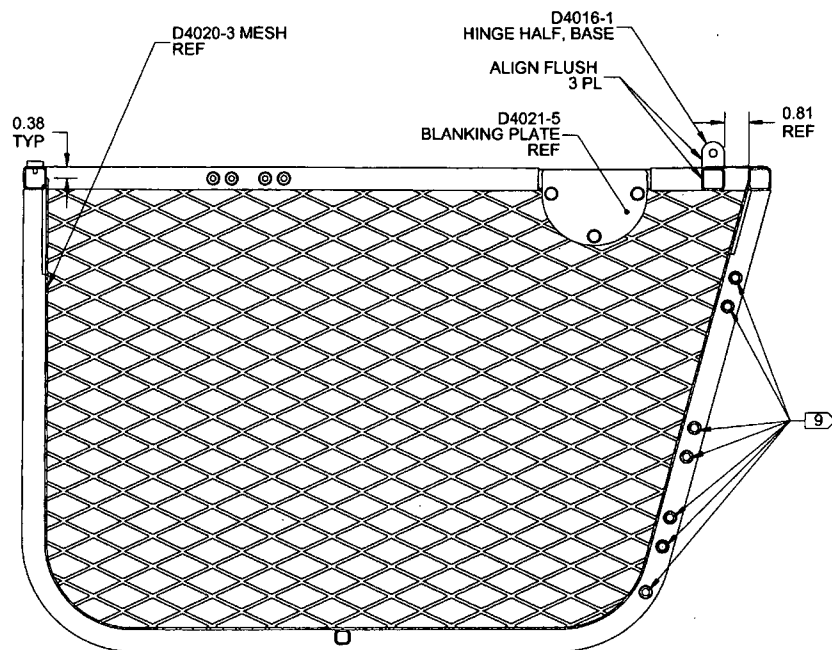

SECTION A-A A5-2

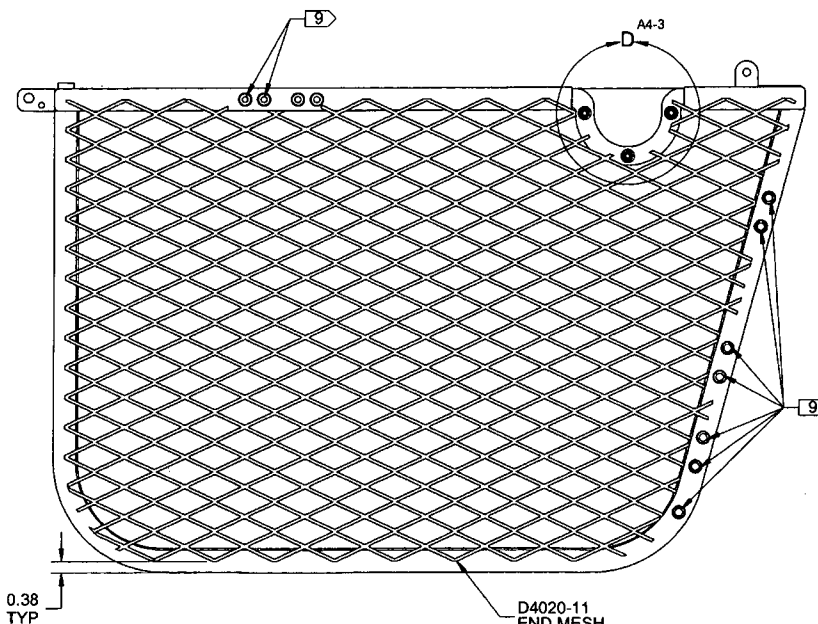

VIEW B-B A2-2

8
D4021-5
BLANKING PLATE

8
AN3-10A BOLT, MACHINE
NAS1149F0332P WASHER, 2X
MS21042L3 NUT
3 PL

TRIM MESH LOCALLY
Ø0.50 - Ø0.60
TO CLEAR FASTENERS

DETAIL D D1-3
B7-2

RELEASED
2013-08-16
WP

DESIGN	AJS	DART AEROSPACE LTD	
DRAWN	AJS	HAWKESBURY, ONTARIO, CANADA	
CHECKED	JP	DRAWING NO.	REV. E
MFG. APPR.		D4017	SHEET 3 OF 5
APPROVED		TITLE	SCALE
DE APPR.		SHORT BASKET BASE ASSY (350) NTS	
DATE	13.07.18	COPYRIGHT © 2010 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR DISCLOSED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

8

7

6

5

4

3






2

1

A

A


ITEM	QTY -101	P/N	DESCRIPTION
	X	D4017-101	TUBULAR ASSY (350 SHORT BASKET)
1	1	D4017-1	RIB
2	1	D4017-3	RIB
3	1	D4017-5	HINGE RIB
4	3	D4017-7	RIB
5	2	D4017-9	RIB
6	1	D3916-5	LIGHT RIB
7	2	D3916-041	RIB ASSY
8	1	D4034-041	AFT UPPER RIB ASSY
9	1	D4034-043	FWD UPPER RIB ASSY

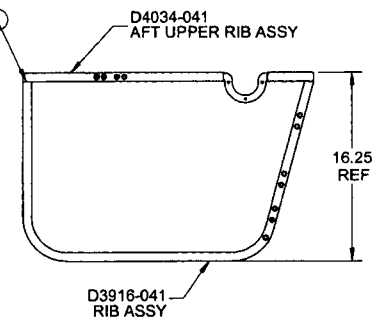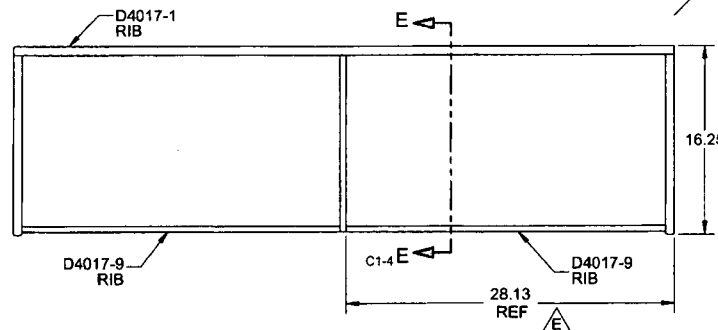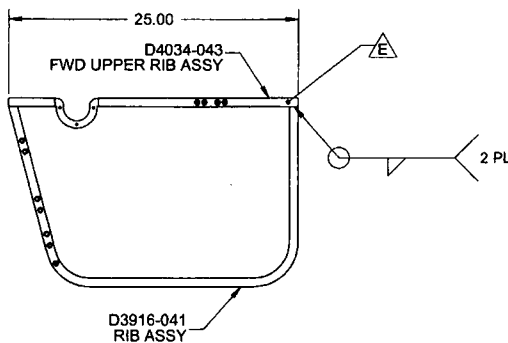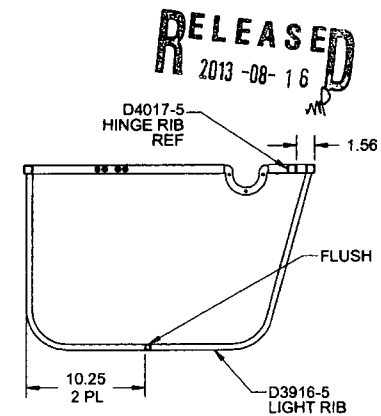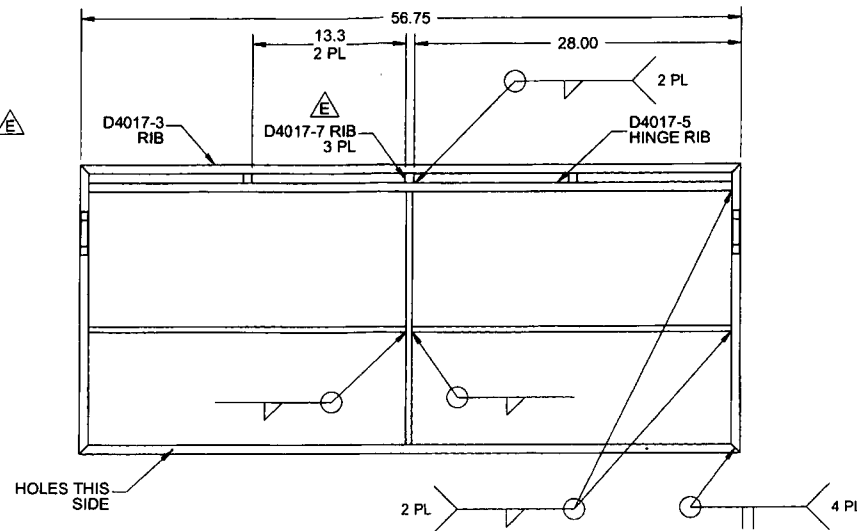

8 D4017-101 TUBULAR ASSY (350 SHORT BASKET)

- NOTES:
- 1) MATERIAL: N/A
 - 2) FINISH: NONE
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: N/A
 - 7) WEIGHT: 15.38 lbs
 - 8) TOLERANCE FOR XX.XX DIMENSIONS ± 0.06 FOR D4017-101
 - 9) WELD PER DART QSI 004

DESIGN	AJS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AJS		
CHECKED	<i>[Signature]</i>	DRAWING NO. D4017	REV. E SHEET 4 OF 5
MFG. APPR.	<i>[Signature]</i>	TITLE SHORT BASKET BASE ASSY (350)	SCALE NTS
APPROVED	<i>[Signature]</i>	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMPILED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
DE APPR.	<i>[Signature]</i>	DATE 13.07.18	

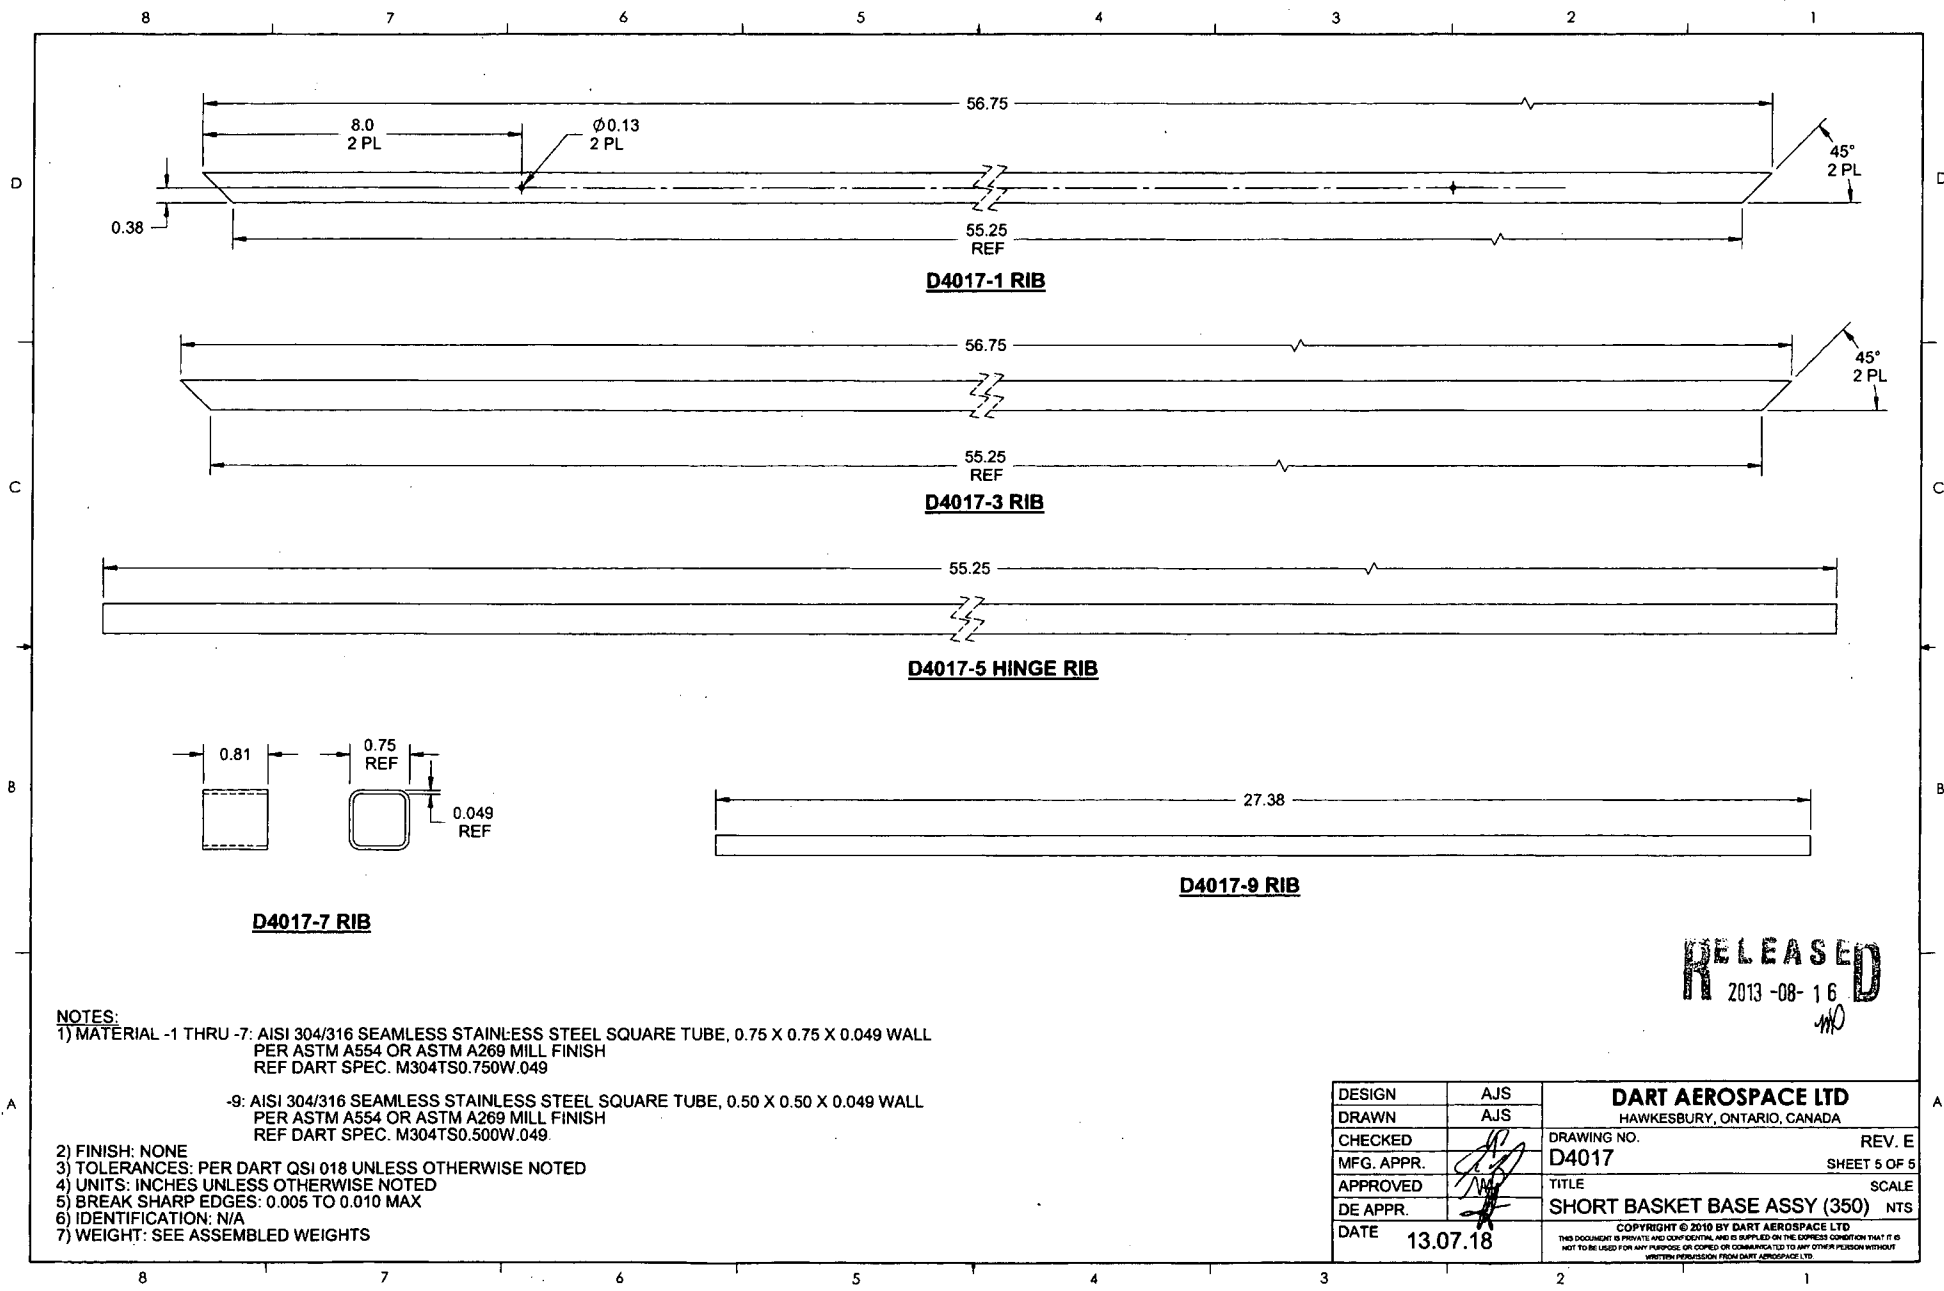

NOTES:

1) MATERIAL -1 THRU -7: AISI 304/316 SEAMLESS STAINLESS STEEL SQUARE TUBE, 0.75 X 0.75 X 0.049 WALL
PER ASTM A554 OR ASTM A269 MILL FINISH
REF DART SPEC. M304TS0.750W.049

-9: AISI 304/316 SEAMLESS STAINLESS STEEL SQUARE TUBE, 0.50 X 0.50 X 0.049 WALL
PER ASTM A554 OR ASTM A269 MILL FINISH
REF DART SPEC. M304TS0.500W.049

- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: SEE ASSEMBLED WEIGHTS

RELEASED
2013-08-16

DESIGN	AJS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AJS		
CHECKED	<i>[Signature]</i>	DRAWING NO. D4017	REV. E
MFG. APPR.	<i>[Signature]</i>	SHEET 5 OF 5	
APPROVED	<i>[Signature]</i>	TITLE	SCALE
DE APPR.	<i>[Signature]</i>	SHORT BASKET BASE ASSY (350) NTS	
DATE	13.07.18	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSES OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
